
2800 N. SHERIDAN RD | REVISED DEMOLITION SCHEDULE

Atlas Industries Inc. | Activity windows revised October 25, 2026 | Anticipated overall completion: January 5, 2027

40% COMPLETE
Above-ground demolition - last reported Oct 21

100% COMPLETE
Tree removal - completed Oct 17

JANUARY 5, 2027
All five client milestones targeted

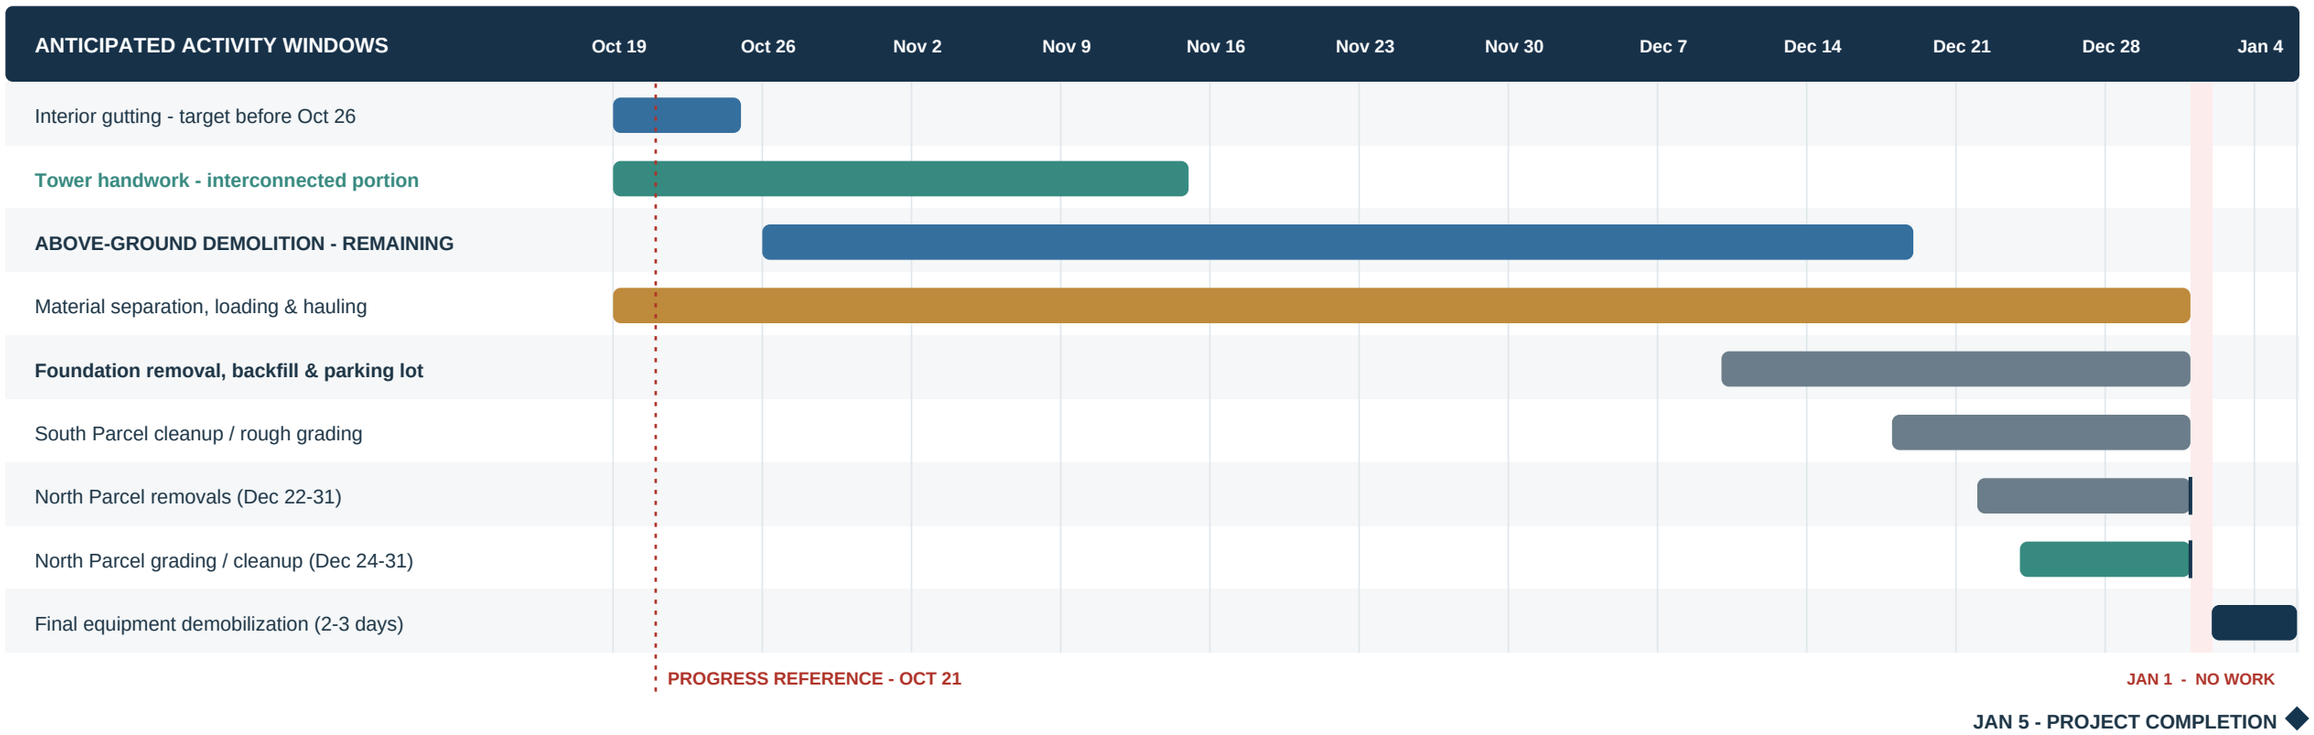

SCHEDULE BASIS / QUALIFICATION

Activity windows reflect the current anticipated sequence; individual dates are planning forecasts, not independent interim completion commitments. Tower handwork and above-ground demolition may overlap where practical. Actual sequencing may change as existing structural conditions are exposed. Material separation and hauling continue alongside demolition. North Parcel removal and grading extend through Dec 31. Foundation, backfill and site work target Dec 31. Nonworking federal holidays: Nov 11, Nov 26, Dec 25, and Jan 1. *40% progress last reported Oct 21. Interior gutting is targeted ahead of Oct 26 structural demolition; field confirmation pending.
